



— HOW-TO GUIDE • PROGRESS BILLING

BILL THE JOB. TRACK THE HOLDBACK.

Build your schedule of values once, put in a claim every month in minutes, bring in approved change orders, and always know what you've billed, what you've been paid and what's still held back.

SET UP

Template, first claim, holdback

CLAIM

By percent or by amount

TRACK

Every dollar of holdback

HOW IT WORKS

Before you bill, open the project's **settings** and fill in the **contract value**, **contract number** and **contract date**. Then open **Progress Billing** from the main menu.

1 The dashboard

2 Start billing

3 Inside the project

4 Schedule of values

5 Change orders

6 Amount due and reconciliation

7 Holdback tracker

Projects									
PROJECT	CLAIMS	LATEST CLAIM	CONTRACT	NET RECEIVED	UNBILLED	HOLDBACK	OWED TO GC	% COMPLETE	ACTION
Westview Plaza Unit 4 Archived 1420 River Road NE, Calgary, AB T2E 0A1	2	#2 — 2026-06-21	\$17,678.00	\$15,910.20	-\$0.00	\$1,767.80	\$0.00	100.0%	Open →
Riverside Water Plant Calgary, AB, Canada	6	#6 — 2026-09-24	\$182,810.63	\$135,446.00	\$32,315.07	\$15,049.56	\$0.00	90.2%	Open →
Parkview Bldg "B" 2210 Crowchild Trail NW, Calgary, AB T2M 3Y7	4	#4 — 2026-09-14	\$132,248.97	\$119,024.07	\$0.00	\$0.00	\$0.00	100.0%	Open →
Southgate Mixed Use Archived 98 Southgate Blvd SE, Calgary, AB T2Z 4K2	2 draft	#2 — 2026-07-27	\$94,654.00	\$0.00	\$94,654.00	\$0.00	\$0.00	0.0%	Open →
Market Square Unit 12 Archived 3150 Market Square NE, Calgary, AB T3J 0R4	2	#2 — 2026-07-10	\$36,059.70	\$32,453.73	\$0.00	\$0.00	\$0.00	100.0%	Open →
Westside QSR Archived 725 Westside Drive SW, Calgary, AB T3H 2L9	3	#3 — 2026-07-16	\$36,415.10	\$32,773.59	\$0.00	\$3,641.51	\$0.00	100.0%	Open →
Poplar Health Clinic Archived 4410 Macleod Trail SW, Calgary, AB T2G 0A3	5	#5 — 2026-05-20	\$60,818.36	\$55,479.38	-\$0.00	\$0.00	\$0.00	100.0%	Open →
Northgate Retail Unit 6120 Northgate Road NE, Calgary, AB T2K 5T1	4	#4 — 2026-09-21	\$96,875.27	\$87,187.74	-\$0.00	\$9,687.53	\$0.00	100.0%	Open →
Downtown Office Fit-Out Archived 505 7th Avenue SW, Calgary, AB T2P 0Y8	4	#4 — 2026-09-08	\$69,458.00	\$64,583.00	\$4,875.00	\$0.00	\$0.00	100.0%	Open →

01


THE DASHBOARD

PROGRESS BILLING

ADMIN

Every job you're billing, and where the money sits.

- 01 Five numbers on top: **Active Projects**, **Total Contract Value**, **Net Received**, **Unbilled Work** and **Holdback Outstanding**.
- 02 Each project shows its **claims**, **latest claim**, **contract**, **net received**, **unbilled**, **holdback**, **owed to GC** and **% complete**.
- 03 Press **Open** to go into a project.

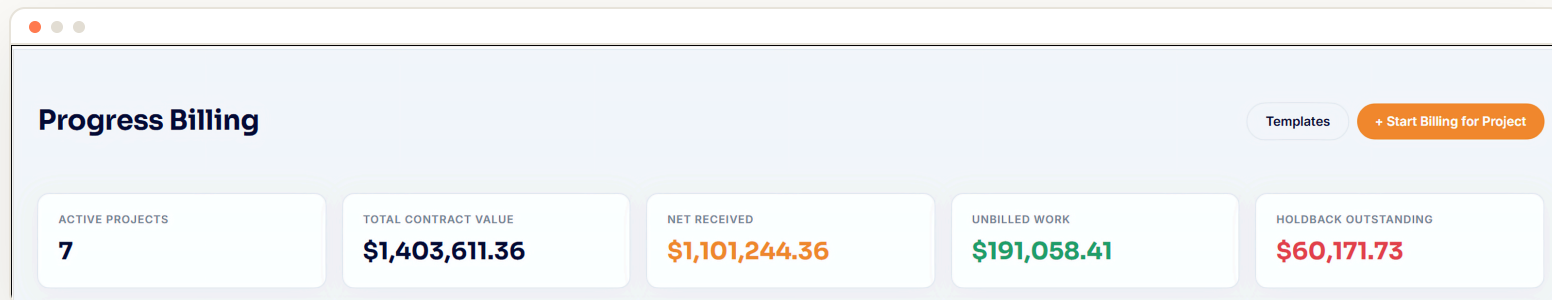

02

START BILLING

START BILLING FOR PROJECT

Set up a job for billing in one window.

- 01 Press **+ Start Billing for Project** and pick the **project**.
- 02 Load an **SOV template** so every line item goes in at once. You can edit them after.
- 03 Set the **claim date** and an optional **period label**.
- 04 Set the **holdback %** for your province or state, and a **warranty holdback %** if the contract has one.
- 05 Press **Create First Claim**.

Start Progress Billing

×

Select a project to start its first claim

Project ▾

SOV Template (optional) ▾

Loads prebuilt line items into the project SOV. You can edit after.

Claim Date
2026-09-30 📅

Period Label (optional)

Holdback %
10

Warranty Holdback %

Optional. Held back through the warranty period.

Cancel>Create First Claim

03

INSIDE THE PROJECT

CLAIM

Every claim on the job, in order.

- 01 Each claim shows its **date**, **amount** and **status**. Approved claims are **locked**.
- 02 The **customer**, **project**, **subcontract PO #** and **contract amount**.
- 03 **Claim details**: date, period label, invoice #, holdback % and warranty holdback %. Use **+ New Claim** each billing period.

-- Back

+ New Claim
Export PDF

Claim #6

Claim #6 Sep 24, 2026 \$12,972.17 SUBMITTED - PENDING APPROVAL	Claim #5 Jun 24, 2026 \$15,803.64 APPROVED	Claim #4 May 25, 2026 \$10,363.58 APPROVED	Claim #3 Apr 27, 2026 \$37,700.24 APPROVED	Claim #2 Mar 23, 2026 \$29,765.58 APPROVED	Claim #1 Feb 25, 2026 \$41,812.96 APPROVED
---	---	---	---	---	---

CUSTOMER Prairie Build Group 1420 River Road NE, Calgary, AB T2E 0A1, Canada	PROJECT Riverside Water Plant Calgary, AB, Canada	SUBCONTRACT PO # 2601-00417	CONTRACT AMOUNT \$129,424.00
--	---	--	---

Claim Details

Date 2026-09-24	Period Label	Invoice #
Holdback % 10	Warranty Holdback % Held back through the warranty period. Released after warranty obligations are satisfied.	

04

SCHEDULE OF VALUES

SOV

Bill by percent or by dollar amount.

- 01 Set a **\$ value** on every line. The lines must add up to the **contract amount**.
- 02 Type a **% complete** on a line, or a dollar amount in **This Claim**. The other fills itself in.
- 03 **Prev. Invoiced** and **Invoiced to Date** keep the running totals.

Schedule of Values SOV locked						
#	DESCRIPTION	\$ VALUE	% COMPLETE	THIS CLAIM	PREV. INVOICED	INVOICED TO DATE
1	Mobilization/Demobilization	\$4,189.51	100.00%	\$0.00	\$4,189.51	\$4,189.51
2	Engineered Shop Drawings - Steel Stud	\$850.00	100.00%	\$0.00	\$850.00	\$850.00
3	Submittals	\$939.00	100.00%	\$0.00	\$939.00	\$939.00
4	Supply & Install - Steel Stud Interior Partition Walls	\$47,553.20	100.00%	\$0.00	\$47,553.20	\$47,553.20
5	Supply & Install - Gypsum Interior Partition Walls	\$54,219.12	100.00%	\$0.00	\$54,219.12	\$54,219.12
6	Supply & Install - Batt Insulation Interior Partition Walls	\$10,960.98	100.00%	\$0.00	\$10,960.98	\$10,960.98
7	Supply & Install - Acoustic Grid / Ceiling	\$9,030.19	80.00	0.00	\$7,224.15	\$7,224.15
8	Closeout Documentation	\$1,500.00	0.00	0.00	\$0.00	\$0.00
Original Contract Sub-total		\$129,242.00	97.44%	\$0.00	\$125,935.96	\$125,935.96
CONTRACT AMOUNT		SOV THIS CLAIM		SOV INVOICED TO DATE		
\$129,424.00		\$0.00		\$125,935.96		

05

CHANGE ORDERS

ADJUSTMENTS

Billed separately from the contract work.

- 01 Take the change order through to **approved** in the project, then bring it in here.
- 02 Bill it the same way, by **percent** or by **amount**.
- 03 Add a **Credit**, **Back Charge** or **Allowance** when you need one.

Change Orders / Adjustments (Billed Separately)							
These items are billed under separate documents and are not included in the Contract Work payable below.							
REF	TYPE	DESCRIPTION	\$ VALUE	% COMPLETE	THIS CLAIM	PREV. INVOICED	INVOICED TO DATE
CO-PR2025027-001 approved	Change Order	RFI 160 & West Wall Furring Tall C	\$18,438.60	100.00%	\$0.00	\$18,438.60	\$18,438.60
CO-PR2025027-002 approved	Change Order	Shower Drywall replacement	\$795.00	100.00%	\$0.00	\$795.00	\$795.00
CO-PR2025027-003 approved	Change Order	Columns and Beam framing	\$20,641.03	50.00	10320.52	\$0.00	\$10,320.52
CO-PR2025027-004 approved	Change Order	Mezzanine - Bottom knee wall	\$8,186.00	50.00	4093.00	\$0.00	\$4,093.00
Not Assigned approved	Change Order	CCN 009	\$5,326.00	100.00%	\$0.00	\$5,326.00	\$5,326.00
ADJUSTMENTS SUMMARY							
Previously Billed			\$24,559.60				
This Claim			\$14,413.52				
Adjustments Invoiced to Date			\$38,973.12				
Total Approved Adjustments			\$53,386.63				

06

AMOUNT DUE AND RECONCILIATION

SUMMARY

The numbers the GC wants to see.

- 01 This claim, less holdback, gives the amount due.
- 02 Original contract sum, net approved adjustments and the revised contract sum.
- 03 Invoiced to date, holdback retained and the **balance to complete**.

CONTRACT WORK (SOV)	
This Claim	\$0.00
Less 10% Holdback	-\$0.00
Contract Work Payable	\$0.00
Amount Due This Claim	\$0.00
PROJECT RECONCILIATION (all billing streams)	
Original Contract Sum	\$129,424.00
Net Approved Adjustments	+\$53,386.63
Revised Contract Sum	\$182,810.63
Contract Work Invoiced to Date	\$125,935.96
Adjustments Invoiced to Date	\$38,973.12
Gross Invoiced to Date	\$164,909.08
Less Total Holdback Retained	-\$16,490.90
Net Invoiced to Date	\$148,418.18
Balance to Complete	\$17,901.55

This section summarizes all billing streams for reference. COs and other adjustments are billed on separate PDFs.

07

HOLDBACK TRACKER

HOLDBACK

Every dollar held back, claim by claim.

- 01 Holdback on every **claim** and every **change order**.
- 02 Tick **Collected** when it's paid. **Export Holdback PDF** for your records.
- 03 **Finalize and sign** the claim to unlock the PDF, then **Approve & Lock** once it's accepted.

Holdback Tracker				
↓ Export Holdback PDF				
DOCUMENT	DATE	BILLED	HOLDBACK	COLLECTED
Claim #1	Feb 25, 2026	\$46,458.84	\$4,645.88	☐
Claim #2	Mar 23, 2026	\$33,072.87	\$3,307.29	☐
Claim #3	Apr 27, 2026	\$41,889.16	\$4,188.92	☐
Claim #4	May 25, 2026	\$4,515.09	\$451.51	☐
CO-PR2025027-001 #4	May 25, 2026	\$7,000.00	\$700.00	☐
Claim #5	Jun 24, 2026	\$0.00	\$0.00	☐
CO-PR2025027-001 #5	Jun 24, 2026	\$11,438.60	\$1,143.86	☐
CO-PR2025027-002 #5	Jun 24, 2026	\$795.00	\$79.50	☐
Not Assigned #5	Jun 24, 2026	\$5,326.00	\$532.60	☐
Claim #6 Pending Approval	Sep 24, 2026	\$0.00	\$0.00	☐
CO-PR2025027-003 #6	Sep 24, 2026	\$10,320.52	\$1,032.05	☐
CO-PR2025027-004 #6	Sep 24, 2026	\$4,093.00	\$409.30	☐
TOTAL		\$164,909.08	\$16,490.91	
Collected: \$0.00 Outstanding: \$16,490.91				
Workflow: Finalize & sign the claim to certify the work and unlock the PDF. Approve & lock once it has been accepted internally.				
Approve & Lock				

— PROGRESS BILLING

NEED A HAND? WE'VE GOT YOU.

Want help loading your first schedule of values or setting up a template? Send us an email and our team will get back to you.

support@subtradesoftware.com



SUBTRADE SOFTWARE LTD. • CALGARY, ALBERTA • SUBTRADESOFTWARE.COM
